ID	Task Name	Duration	Start	Finish
1	Receive Bids	10 days	5/13	5/26
2	Issue Contracts Letters of Intent	1 day	5/27	5/27
3	Fabrication Steel	15 days	5/30	6/17
4	Fabrication Rebar	5 days	5/30	6/3
5	Purchase Lift Station	2 days	5/30	5/31
6				
7	**School Out**	0 days	6/13	6/13
8				
9	Demo Clear Site	2 days	6/13	6/14
10	Install Footings	3 days	6/15	6/17
11	Install Lift Station Pit	3 days	6/15	6/17
12	Install Plumbing Underground	2 days	6/20	6/21
13	Install Electrical Feed	2 days	6/20	6/21
14	Masonry Stem Walls	2 days	6/20	6/21
15	Backfill Prep and Pour Slab	3 days	6/22	6/24
16	Masonry Walls	6 days	6/27	7/5
17	Set Steel Frames	2 days	7/6	7/7
18	Install Steel Stud Joists	3 days	7/8	7/12
19	Install Deck	3 days	7/13	7/15
20	Install Facia Soffit and Metal Roof	5 days	7/18	7/22
21	Interior Plumbing Rough	6 days	7/18	7/25
22	Interior Electrical Rough	6 days	7/18	7/25
23	Paint Interior Deck	1 day	7/25	7/25
24	Install Doors	2 days	7/26	7/27
25	Paint Interior Walls	3 days	7/26	7/28
26	Epoxy Floor	4 days	7/29	8/3
27	Install Accessories	2 days	8/4	8/5
28	Trim Out MEP	3 days	8/4	8/8
29	Punch and Clean	5 days	8/9	8/15
30				
31	**School Begins**	0 days	8/15	8/15

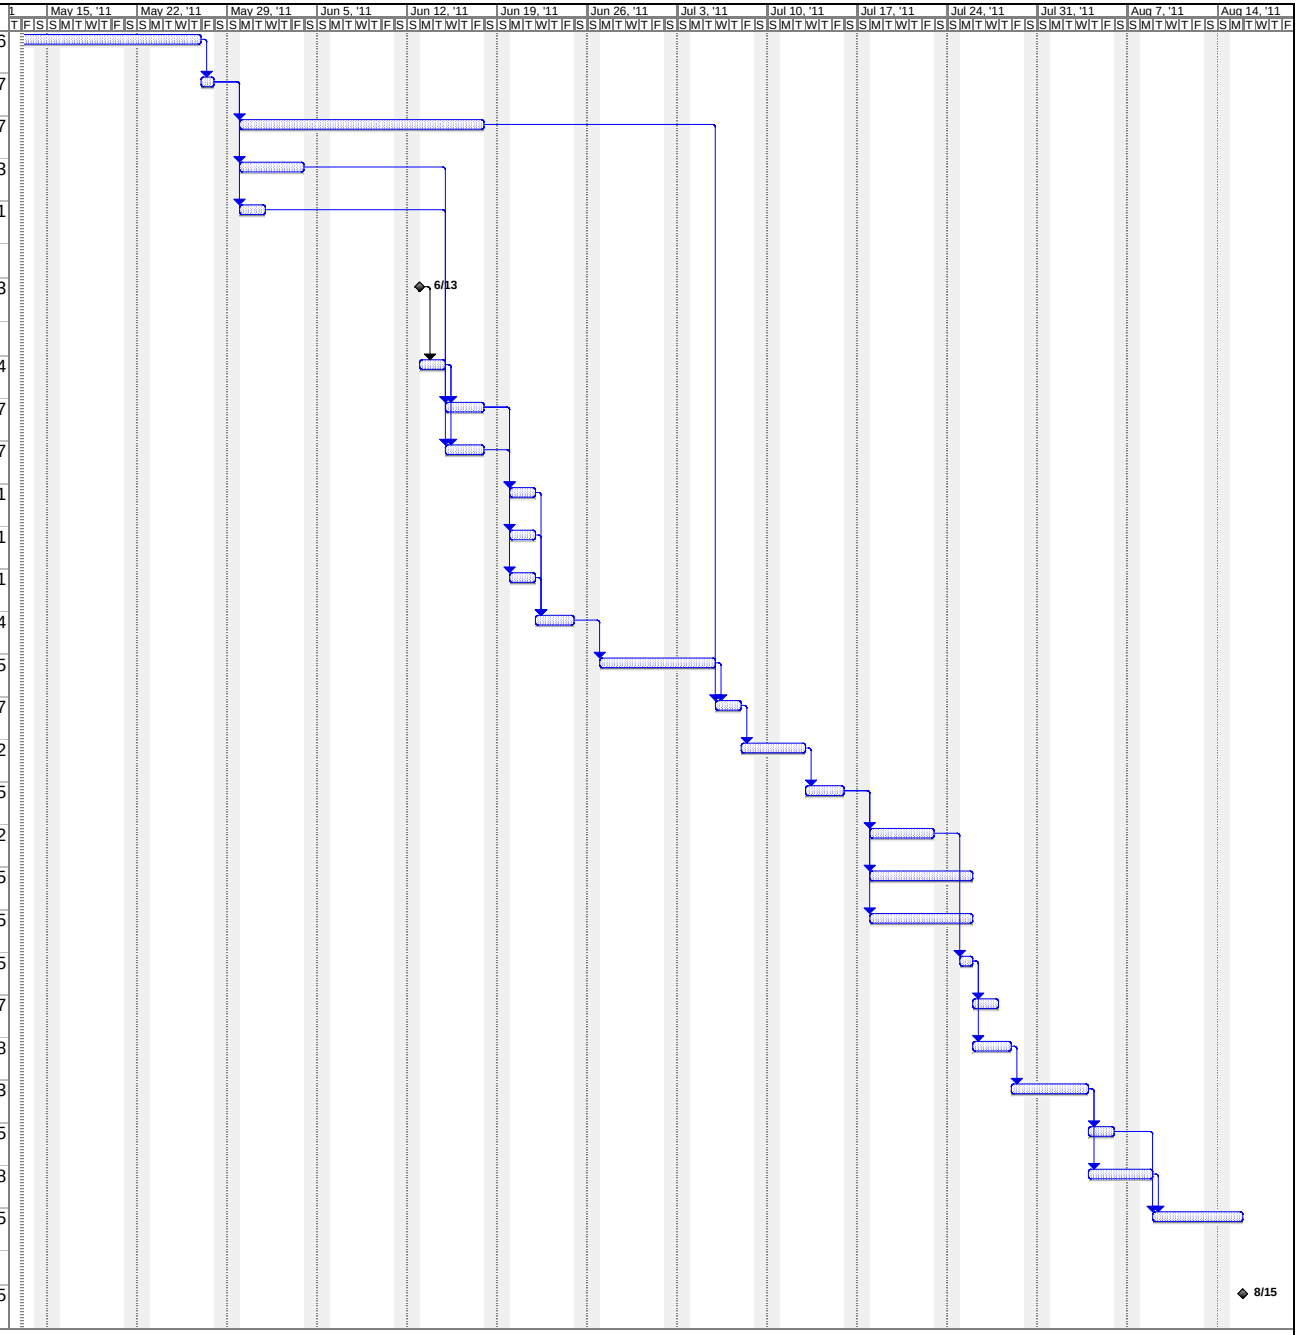

Project: SIGSBEE RESTROOM
Date: 5/13

Task Progress Milestone
